

Improvements for Potter Street, Ellis Street/Haddonfield-Berlin Road and Kresson Road
Project Update No. 3
July 15, 2011

Work Completed the Week of July 11:

The installation of sections of new water main and sanitary sewer main repairs were completed. Curb work along Ellis and Potter Streets was completed with sidewalk installation along both streets and driveway apron replacement on Potter Street commencing. The lowering of MacDonald Park to rough grade was completed including excavation of pending retaining wall, and construction of the wall on Potter adjacent to the Haddonfield Little League fields began.




Sidewalk Construction Along Ellis Street Adjacent to HLL Fields



Retaining Wall Construction On Potter St. Adjacent to HLL Fields

Anticipated Work for the Week of July 18:

Retaining wall construction will resume on Potter Street and begin along Ellis. Sidewalk and driveway apron construction along both roads will continue.

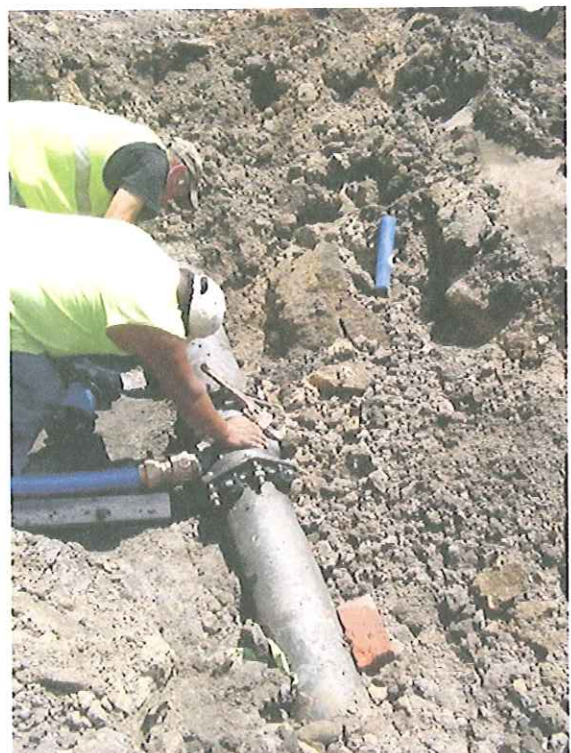

Water Main Installation
