

*HMHS Stadium & Anniversary Fields Improvements
Project Update No. 2
June 28, 2013*

Work Completed During the Weeks of June 17 and 24:

Work was completed on the installation of underdrain pipe and structures on Anniversary Field. Installation of filter fabric, underdrain, field drain coarse stone and perimeter curb for the field began. A subcontractor bored pipe underneath the track to connect the drainage systems between the two fields, and the Contractor began work on Stadium Field by stripping topsoil.




Installation of Filter Fabric, Underdrain and Coarse Stone Layer on Anniversary Field



Stripping of Topsoil on Stadium Field

Work Anticipated the Weeks of July 1 and 8:

Perimeter curb around Anniversary Field will be completed and the installation and fine grading of field stone layer will continue. Stripping of topsoil and grading will continue on Stadium Field with pipe work beginning after the Holiday.

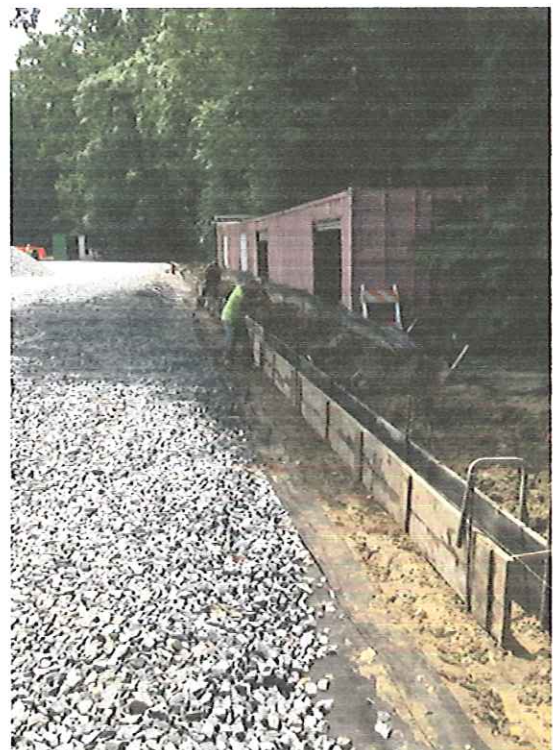

Construction of Perimeter Curb around Anniversary Field
